

Marine Construction Dredging Pile Driving

1501 Taylor Way • Tacoma, Washington 98421

PHONES: Tacoma (253) 254-0118,

Seattle (206) 623-0114,

Fax (253) 254-0155



**AMERICAN
CONSTRUCTION COMPANY**

CONTRACTORS LIC NO. 223-01-AM-ER-IC*372 NO.

DATE January 20, 2011

TO:

Columbia River Crossing Project Office
700 Washington Street, Suite 300
Vancouver, WA 98660

Attn: Frank Green, P.E.

JOB #:

TITLE:

Columbia River Bridge Temporary
Pile Test Program (#8078)

THE FOLLOWING ITEMS ARE BEING SENT:

Herewith

Under Separate Cover

Direct

X

QUANTITY	DESCRIPTION
5 EA	Preliminary Project Schedule

These items are being sent:

- | | |
|---|--|
| X | Per your request |
| X | Please keep us advised of action taken |
| X | For you to process |
| X | For your inspection and approval |
| X | For your general information and file |
| X | For your approval or corrections |

RECEIVED

JAN 21 2011

Columbia River Crossing

REMARKS:

Please contact us promptly if there is a problem or question

COPY TO:


[Empty box for copy to]

AMERICAN CONSTRUCTION COMPANY, INC.

BY:

Vernon Uy

Act ID	Description	Orig Dur	Early Start	Early Finish
1000	NOTICE OF AWARD	0	12JAN11 *	
1005	PROJECT COMPLETION	0	28FEB11 *	
1010	PREPARE SUBMITTALS	8d	12JAN11	21JAN11
1020	ORDER/RECEIVE PIPE PILING	11d	24JAN11	07FEB11
1030	ORDER RECEIVE UNCONFINED BUBBLE	11d	24JAN11	07FEB11
1040	ORDER/RECEIVE CONFINED BUBBLE CURTAIN	11d	24JAN11	07FEB11
1050	MOBILIZE TO LOCATION A	1d	07FEB11	07FEB11
1055	TEST UNCONFINED BUBBLE CURTAIN	1d	08FEB11	08FEB11
1060	INSTALL PILE A-1	1d	08FEB11	08FEB11
1065	TEST CONFINED BUBBLE CURTAIN	1d	09FEB11	09FEB11
1070	INSTALL PILE A-2	1d	09FEB11	09FEB11
1080	INSTALL PILE A-3	1d	10FEB11	10FEB11
1090	INSTALL PILE A-4	1d	10FEB11	10FEB11
1100	MOVE TO LOCATION B	1d	11FEB11	11FEB11
1110	INSTALL PILE B-1	1d	11FEB11	11FEB11
1120	INSTALL PILE B-2	1d	14FEB11	14FEB11
1130	MOVE TO LOCATION A	1d	14FEB11	14FEB11
1140	RESTRIKE PILE A-1	1d	15FEB11	15FEB11
1150	RESTRIKE PILE A-2	1d	15FEB11	15FEB11
1160	RESTRIKE PILE A-3	1d	15FEB11	15FEB11
1170	RESTRIKE PILE A-4	1d	15FEB11	15FEB11
1180	REMOVE A LOCATION PILES	4d	16FEB11	21FEB11
1190	MOVE TO LOCATION B	1d	22FEB11	22FEB11
1200	RESTRIKE PILE B-1	1d	22FEB11	22FEB11
1210	RESTRIKE PILE B-2	1d	22FEB11	22FEB11
1220	REMOVE LOCATION B PILES	2d	23FEB11	24FEB11
1230	DEMOBILIZE	1d	25FEB11	25FEB11

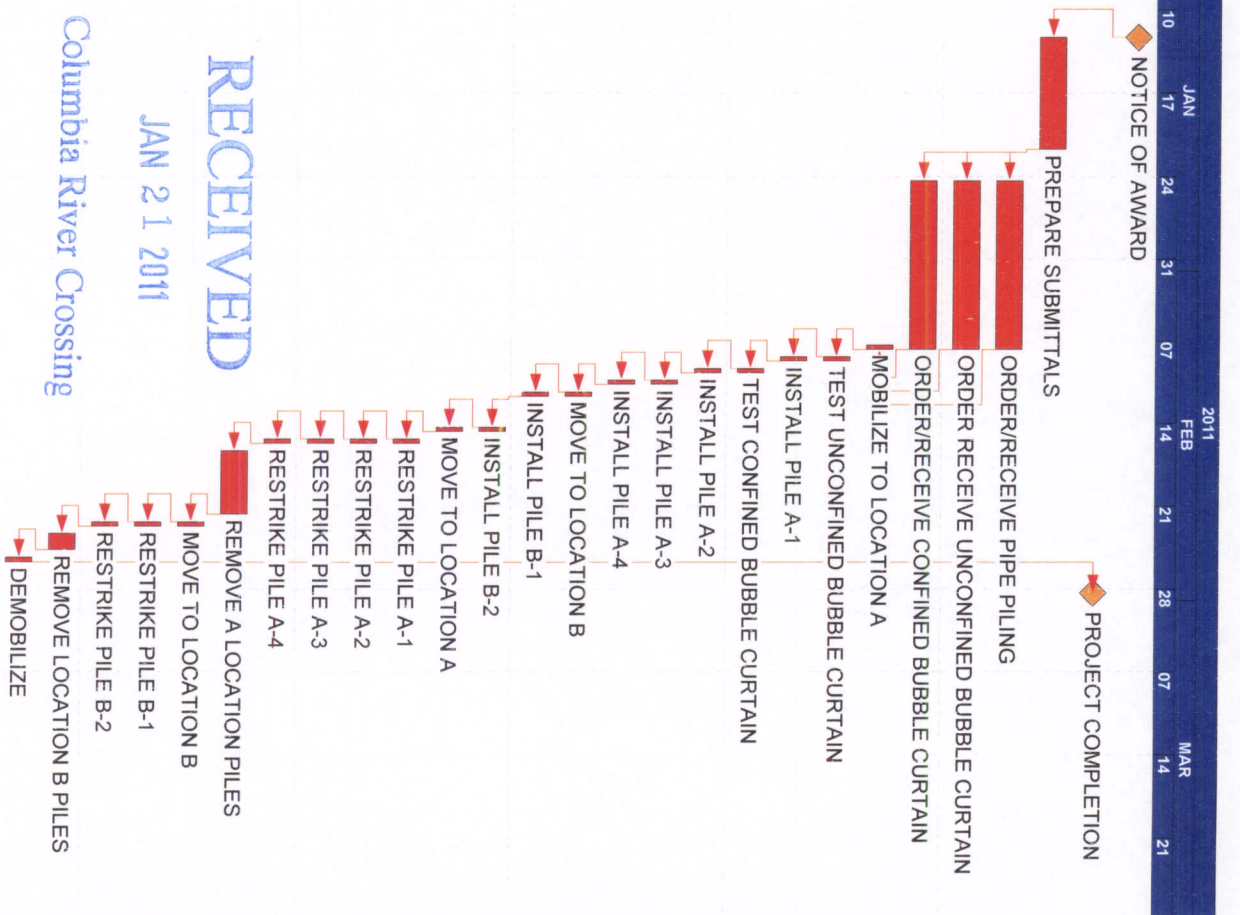

Start date	03JAN11
Finish date	25FEB11
Data date	03JAN11
Run date	20JAN11
Page number	1A
© Primavera Systems, Inc.	

WSDOT
COLUMBIA RIVER BRIDGE TEMPORARY PILE TEST PROGRAM

- Early bar
- Progress bar
- Critical bar
- Summary bar
- ◆ Start milestone point
- ◇ Finish milestone point
